



USAG FRANCONIA

TEAM OF TEAMS



**USAG FRANCONIA
TRANSFORMATION OPLAN BRIEF**



USAG-F MISSION

Effective 29 Jul 05, USAG Franconia executes rebasing and transformation within the USAG Franconia Area Of Responsibility (AOR) in order to successfully support customer campaign plans for transformation IAW directed timelines. USAG Franconia will support tenant unit inactivation, redeployment, and repositioning; maintain service to Soldiers and families throughout the process; support the transition of the civilian workforce; transfer property to EURO; establish and validate three direct report garrisons under the command and control of EURO; and inactivate.



USAG Franconia Commander's Intent

- **Purpose:** To successfully support USAG-F customers in executing GWOT operations, training, force well-being, and Army and USAREUR transformation missions ending in inactivation of USAG-F.

Key Tasks:

- Support tenant unit deployment, redeployment, reintegration, inactivation, return, and restationing.
- Establishing three stand-alone garrisons under C2 of EURO
- Transfer BASEOPS support for garrisons remaining in the Wuerzburg footprint to USAG-S
- Transfer excess real, installation, CFMO, UPH property
- Maintain steadfast focus on the human dimension; the quality of facilities and services provided remains the very best possible until the last soldier/family departs
- Support successful transition of civilian workforce;
- Inactivate USAG-F

End State:

USAG-Franconia successfully inactivated with closing installations in the hands of an EURO closure team or local government; tenant organizations having successfully completed deployment, redeployment, reintegration, inactivation, return or restationing, postured to continue mission at maximum readiness.



CCIR



- Any potential or actual degradation to mission capability (personnel, equipment, facilities) that impacts transformation
- Intent or legal action taken against US Government due to transformation
- Any negative press that potentially could impact transformation
- Any higher HQs policy changes
- Pending closure or closure of facility on USAG Franconia installation
- Any event or action that potentially impacts completion of transformation IAW timeline

TEAM OF



EEFI



- Any information WRT transformation not officially vetted by USAG Franconia Commander
- Details of equipment and troop movements
- Detailed progress reports concerning transformation process



Concept of the Operation

Planning and Preparation (current-Nov 05):

During this phase the USAG Franconia staff will conduct deliberate MDMP ICW tenant units, DODDs Europe, AAFES, DECA and other support agencies IOT develop the road map to support restationing, deployments, redeployments, reintegration, inactivations, and returning units to CONUS.

Support to Tenant Units (Dec 05-Dec 06):

This phase includes R4 and Welcome Home Ceremony support to units currently deployed and support to tenant units that are restationing, inactivating and returning to CONUS while maintaining quality community services to soldiers, and families throughout the transformation process.

TEAM OF



Concept of the Operation

Validation of Direct Reporting Garrisons and transfer of daily operations to USAG Schweinfurt (NLT 1 Oct 06):

During this phase USAG Franconia will establish the validation criteria and conduct the necessary training / rehearsals and left seat / right seat rides IOT successfully transition the direct report Garrisons to EURO NLT 01 OCT 06 and transfer daily operations to USAG Schweinfurt. .

Closure / Inactivation (o/o 15 Oct 06):

During this phase USAG Franconia will continue closure activities IAW USAREUR checklists and inactivate upon completion of closure activities.

TEAM OF



AO WURZ / KITZ / GIEB



FAULENBERG KASERNE

HQs, USAG FRANCONIA
HQs, 106th FINANCE BN
Contracting - Leighton
286 MP - Leighton
DAPS

LARSON BARRACKS

~~17th SIG BN~~
17th SIG BN
147th MAINT CO - ILLESHEIM
PX
38 PSB

HARVEY BARRACKS

DISCOM, 1ID
701st MSB
HEALTH CLINIC
AST KITZINGEN
PX
DECA
12CM-GRAFENWOEHR

LEIGHTON BARRACKS


HQs, 1ID
101st MI BN
1st MP CO
HQ, 69th SIG BN
AST WÜRZBURG
DECA
DODDS
AFN
72nd MED

WÜRZBURG HOSPITAL

67th CBT SPT HOSPITAL
MEDDAC
DENTAC

GIEBELSTADT AAF

HQs, 69th ADA BDE
HQs, 12th AVN BDE
3-158 AVN BN - KATTERBACH
5-158 AVN BN
7-159 AVN BN - ILLESHEIM
3-58 ATS BN - LEIGHTON
HEALTH CLINIC
AST GIEBELSTADT
Shoppette
STOV
DECA
67 FST-LANDSTUHL

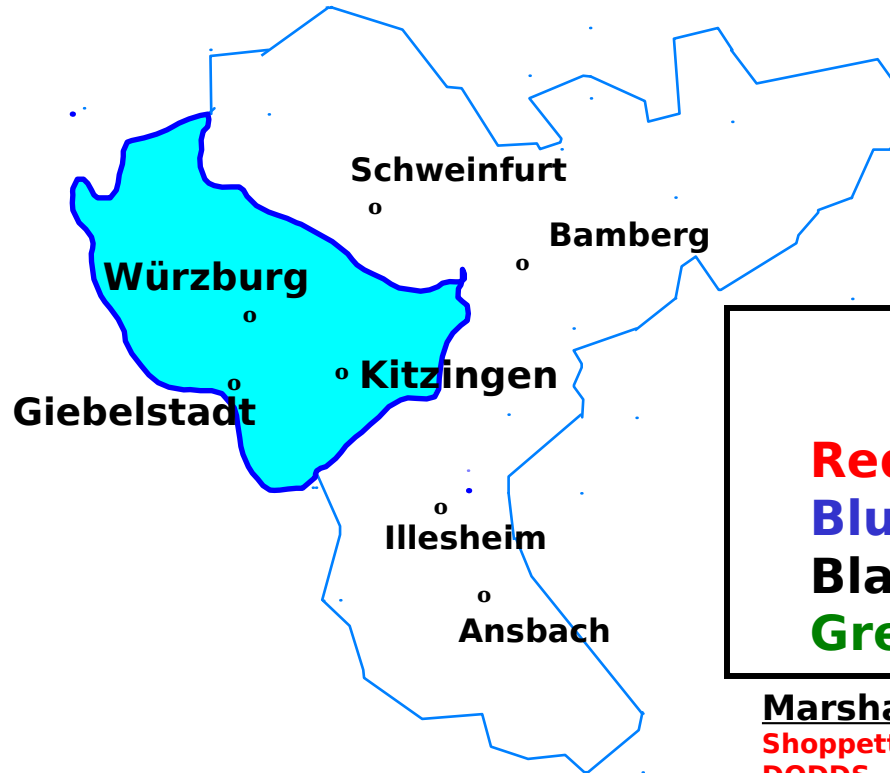

Legend

Red: inactivating
Blue: returning
Black: rebasing
Green: remaining

Marshal Heights

Shoppette
DODDS



Assumptions

- Adequate funding will be available to execute plan through FY07
- Stable civilian work force will be maintained throughout process
- Facilities at gaining installations will be ready for soldiers & family
- Sufficient moving companies available to support movement
- Assignment / movement process will be fixed prior to execution
- Current USAG Franconia staff can remain in place until deactivation



Assumptions (cont)

- Unit inactivation, redeployment, restationing timeline will remain solid
- No other restationing requirements exist currently
- Environmental management requirements will increase
- Soldiers and families will move together
- Adequate storage space is available to support equipment turn-in
- Unforeseen site conditions will exist
- Property accountability will be maintained throughout the process



Time Line for Operation



- See timeline matrix



USAG Franconia Tasks



- See task matrix



RFIs



RFIs	RFI directed to
What is IMA-Es plan for CONUS/OCONUS follow on assignments?	Euro
Confirmation of VERA / VSIP program and its criteria for approval	Euro
How is IMA-E supporting transforming civilian employees from USAG-F?	Euro
When will PPP window open for registration?	Internal
Incentives for retention of critical employees. What, when?	Euro
Time we no longer receive routine taskers (tentatively Jan 06)	Euro
When will units stop supporting DFAC operations?	1ID
Who will fund continued DFAC operations?	Euro
DRMO cleans hard drives, what is their capacity?	DRMO
Disposition of equipment for 17 SIG and 12 AVN from downrange.	Units
Does the 1ID museum and Victory park get packed before or after departure ceremony.	1ID
When do the fire departments stand down?	Euro
When do we remove support from Gieb and Harvy airfields?	Euro
What are the criterion for validation of DRGs?	Internal
What is the disposition of 212 MP PLTs that remain in Kitzingen?	Euro
Status of regional support activities; TISA, Base Ops Maint, AFMIS	Euro
Who is assisting the 72 nd Med Det and 67 th FST w / transformation while deployed?	Unit / Euro
What types of audits/reviews are required for overseas base closures?	Euro
Who is funding Welcome Home Ceremonies?	Euro

TEAM OF

GUIDANCE



TEAM OF
